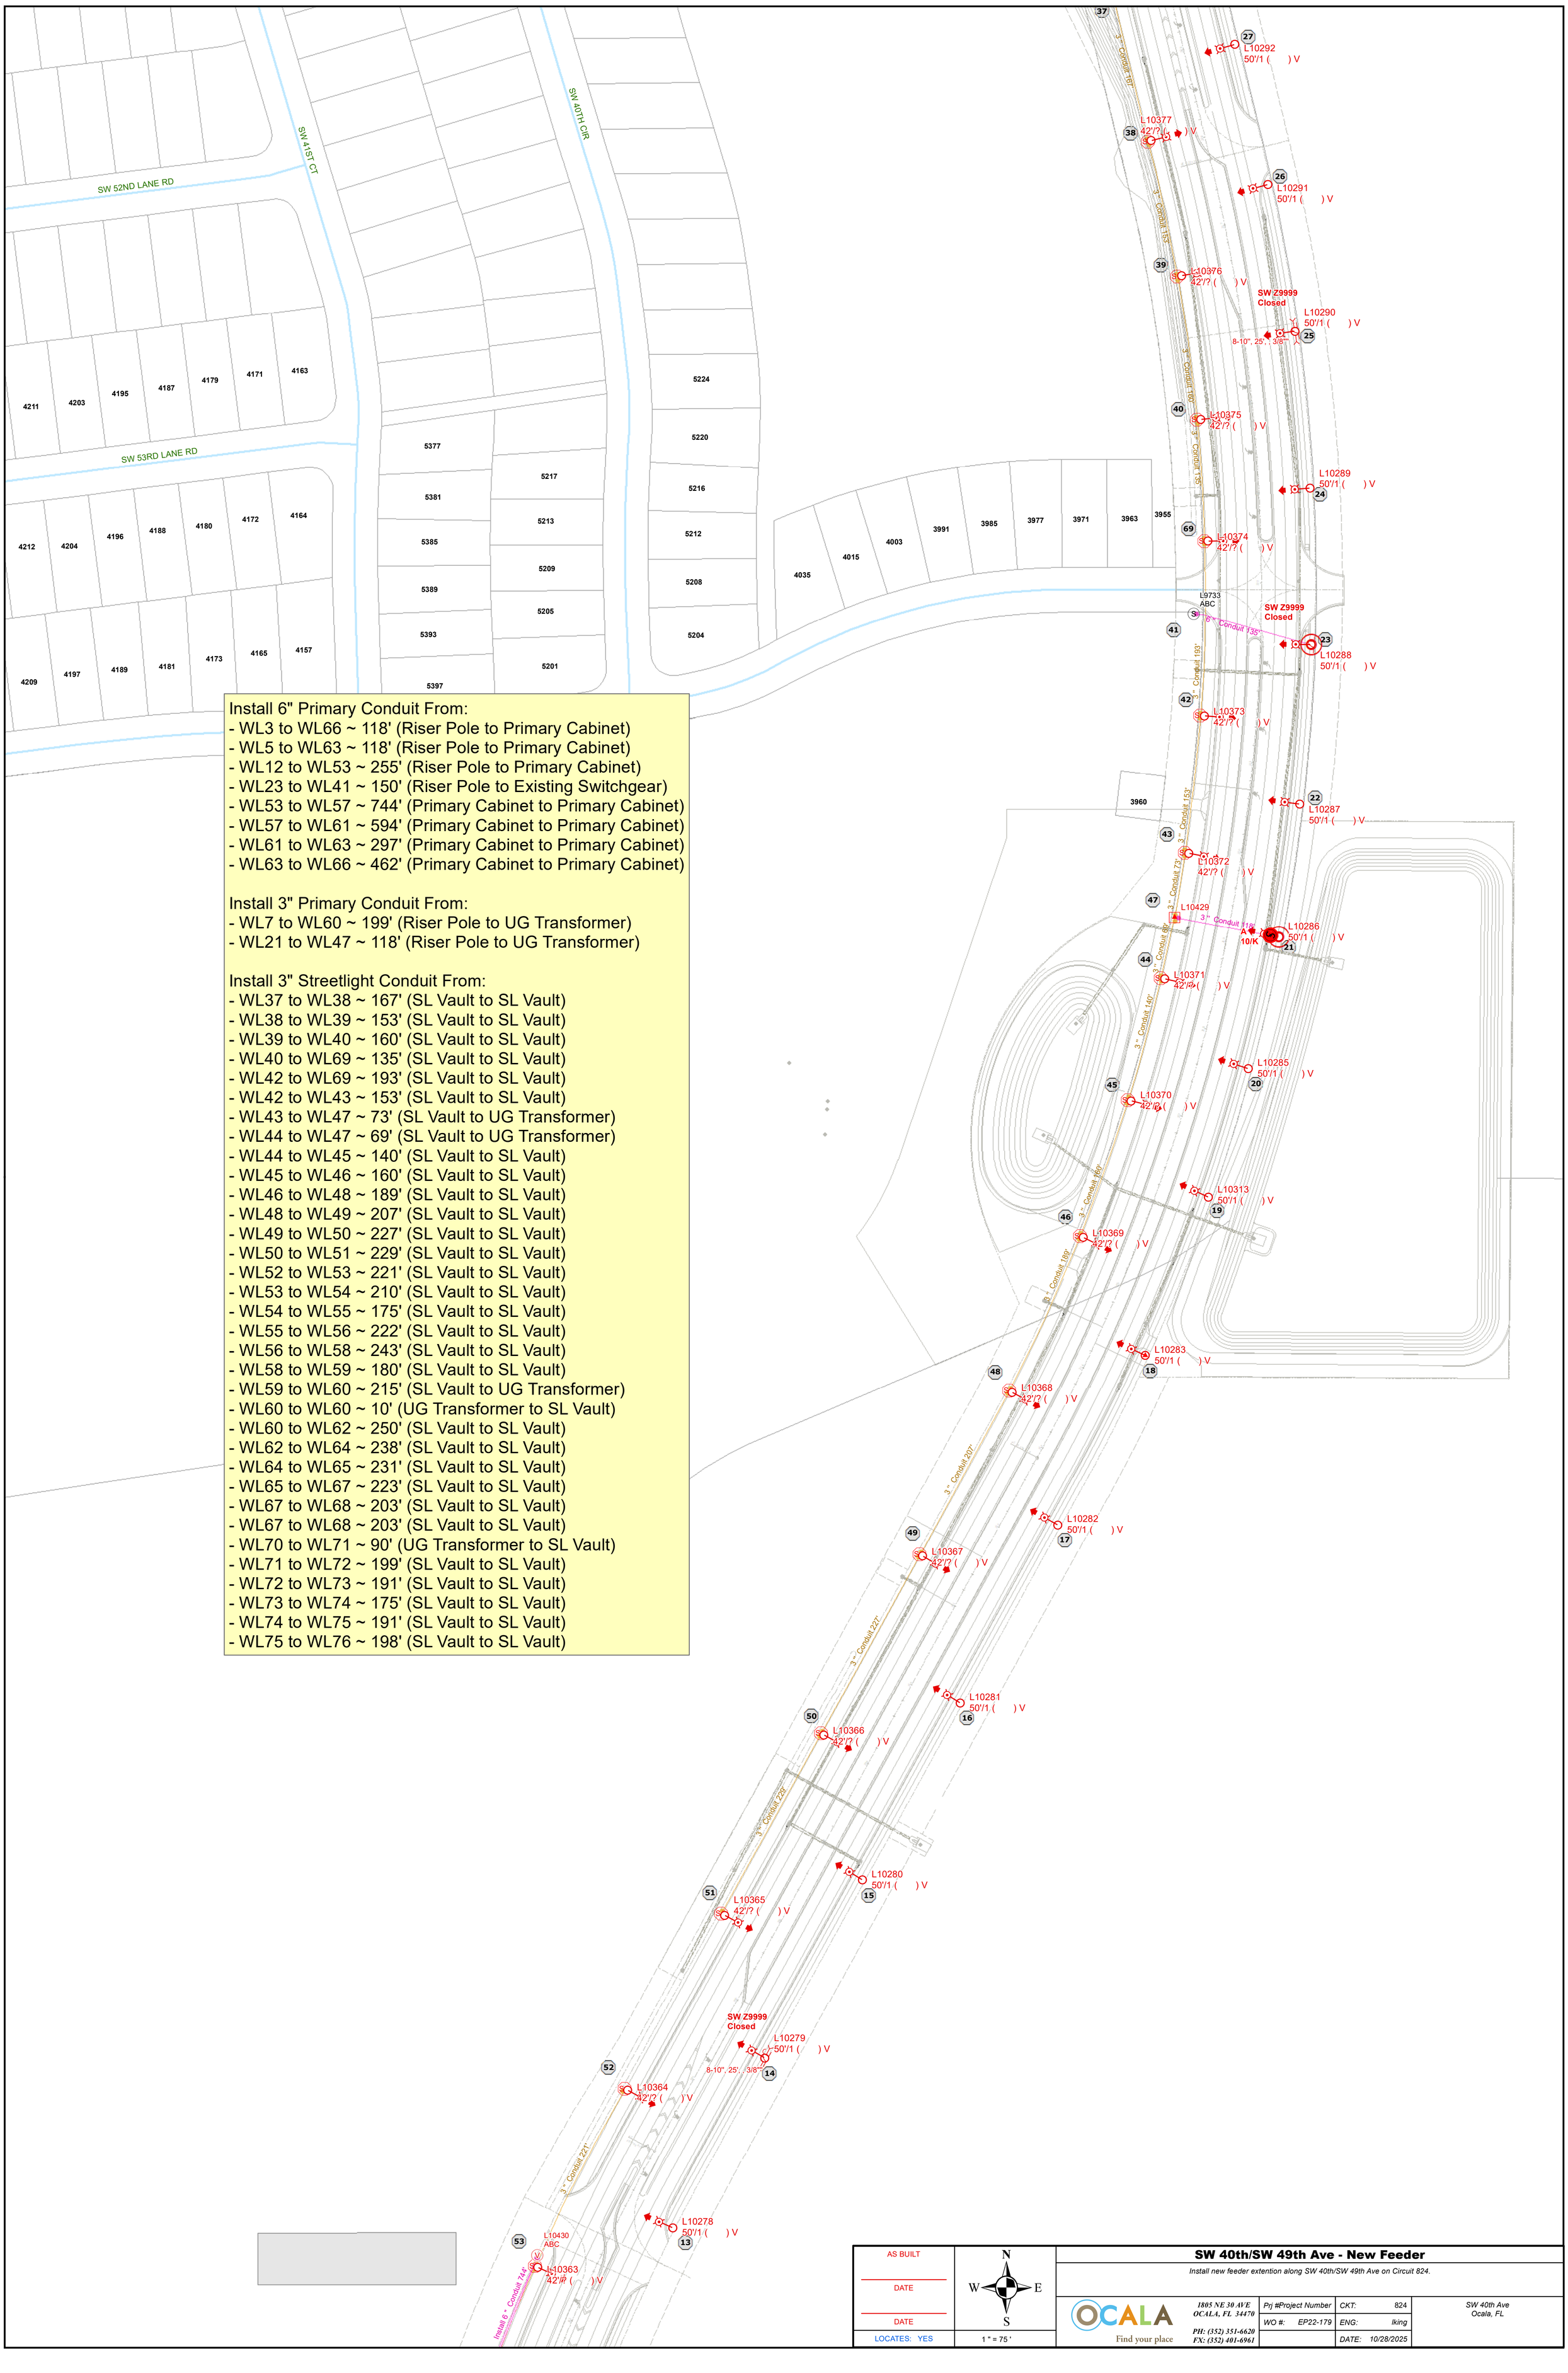


Install 6" Primary Conduit From:
- WL3 to WL66 ~ 118' (Riser Pole to Primary Cabinet)
- WL5 to WL63 ~ 118' (Riser Pole to Primary Cabinet)
- WL12 to WL53 ~ 255' (Riser Pole to Primary Cabinet)
- WL23 to WL41 ~ 150' (Riser Pole to Existing Switchgear)
- WL53 to WL57 ~ 744' (Primary Cabinet to Primary Cabinet)
- WL57 to WL61 ~ 594' (Primary Cabinet to Primary Cabinet)
- WL61 to WL63 ~ 297' (Primary Cabinet to Primary Cabinet)
- WL63 to WL66 ~ 462' (Primary Cabinet to Primary Cabinet)

Install 3" Primary Conduit From:
- WL7 to WL60 ~ 199' (Riser Pole to UG Transformer)
- WL21 to WL47 ~ 118' (Riser Pole to UG Transformer)

Install 3" Streetlight Conduit From:
- WL37 to WL38 ~ 167' (SL Vault to SL Vault)
- WL38 to WL39 ~ 153' (SL Vault to SL Vault)
- WL39 to WL40 ~ 160' (SL Vault to SL Vault)
- WL40 to WL69 ~ 135' (SL Vault to SL Vault)
- WL42 to WL69 ~ 193' (SL Vault to SL Vault)
- WL42 to WL43 ~ 153' (SL Vault to SL Vault)
- WL43 to WL47 ~ 73' (SL Vault to UG Transformer)
- WL44 to WL47 ~ 69' (SL Vault to UG Transformer)
- WL44 to WL45 ~ 140' (SL Vault to SL Vault)
- WL45 to WL46 ~ 160' (SL Vault to SL Vault)
- WL46 to WL48 ~ 189' (SL Vault to SL Vault)
- WL48 to WL49 ~ 207' (SL Vault to SL Vault)
- WL49 to WL50 ~ 227' (SL Vault to SL Vault)
- WL50 to WL51 ~ 229' (SL Vault to SL Vault)
- WL52 to WL53 ~ 221' (SL Vault to SL Vault)
- WL53 to WL54 ~ 210' (SL Vault to SL Vault)
- WL54 to WL55 ~ 175' (SL Vault to SL Vault)
- WL55 to WL56 ~ 222' (SL Vault to SL Vault)
- WL56 to WL58 ~ 243' (SL Vault to SL Vault)
- WL58 to WL59 ~ 180' (SL Vault to SL Vault)
- WL59 to WL60 ~ 215' (SL Vault to UG Transformer)
- WL60 to WL60 ~ 10' (UG Transformer to SL Vault)
- WL60 to WL62 ~ 250' (SL Vault to SL Vault)
- WL62 to WL64 ~ 238' (SL Vault to SL Vault)
- WL64 to WL65 ~ 231' (SL Vault to SL Vault)
- WL65 to WL67 ~ 223' (SL Vault to SL Vault)
- WL67 to WL68 ~ 203' (SL Vault to SL Vault)
- WL67 to WL68 ~ 203' (SL Vault to SL Vault)
- WL70 to WL71 ~ 90' (UG Transformer to SL Vault)
- WL71 to WL72 ~ 199' (SL Vault to SL Vault)
- WL72 to WL73 ~ 191' (SL Vault to SL Vault)
- WL73 to WL74 ~ 175' (SL Vault to SL Vault)
- WL74 to WL75 ~ 191' (SL Vault to SL Vault)
- WL75 to WL76 ~ 198' (SL Vault to SL Vault)

AS BUILT

DATE

DATE

LOCATES: YES

N W E S

1 " = 75 '

SW 40th/SW 49th Ave - New Feeder

Install new feeder extention along SW 40th/SW 49th Ave on Circuit 824.

OCALA Find your place

1805 NE 30 AVE
OCALA, FL 34470
PH: (352) 351-6620
FX: (352) 401-6961

Prj #Project Number	*CKT:*	*824*	*SW 40th Ave Ocala, FL*
WO #: EP22-179	*ENG:*	*lking*	
	DATE:	*10/28/2025*	
